







AGENDA

- Design Update
- Construction Update
- Next Steps








GUIDING DESIGN PRINCIPLES

- Activate Main Street
- Activate Ramseur Street
- Connectivity Between East Durham and Downtown
- Open Space/ Streetscape
- Provide Opportunities for Future Growth and Development
- Incorporate Public Art
- Pedestrian Friendly
- Minimize Surface Parking
- Safety and Security






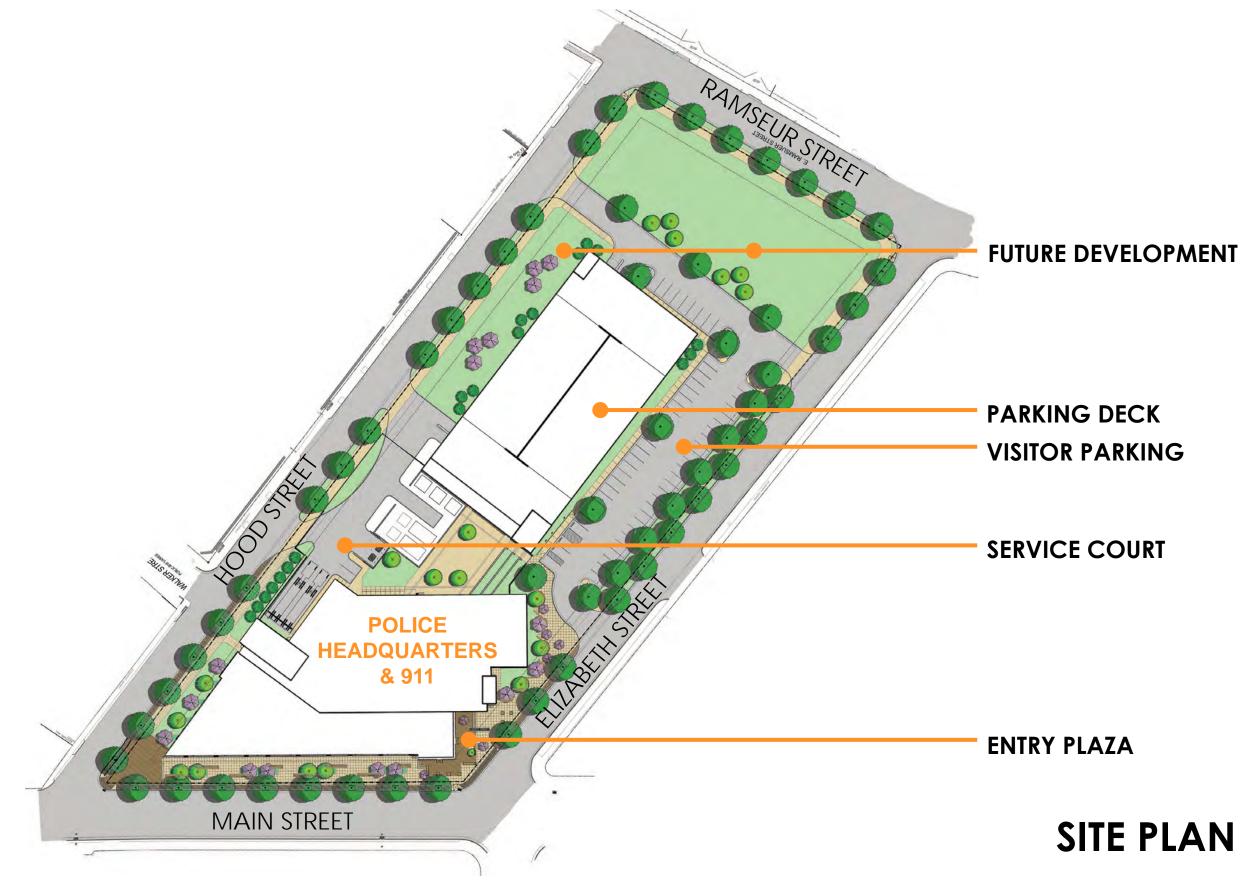










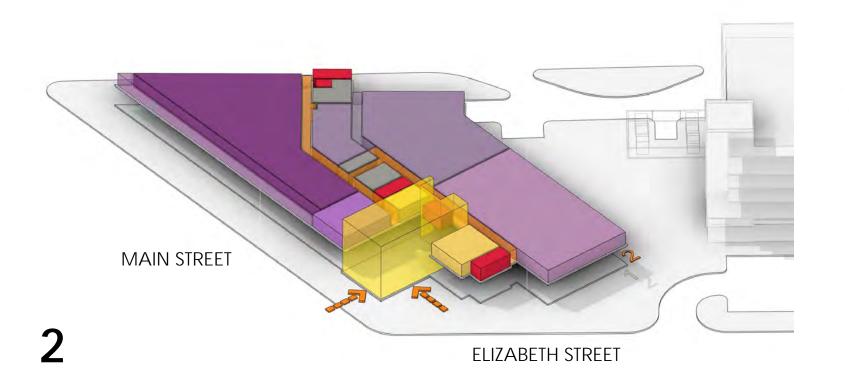

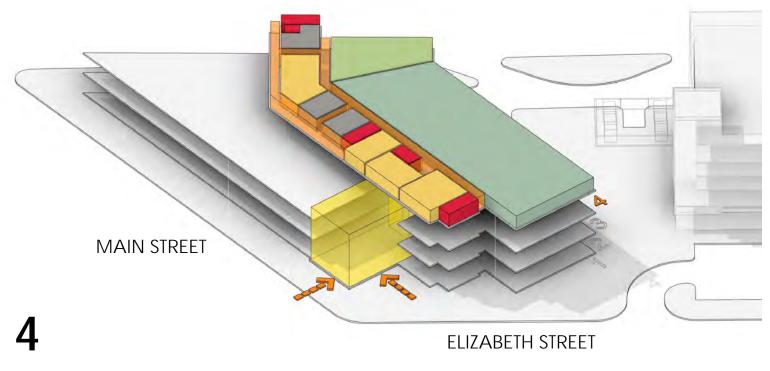

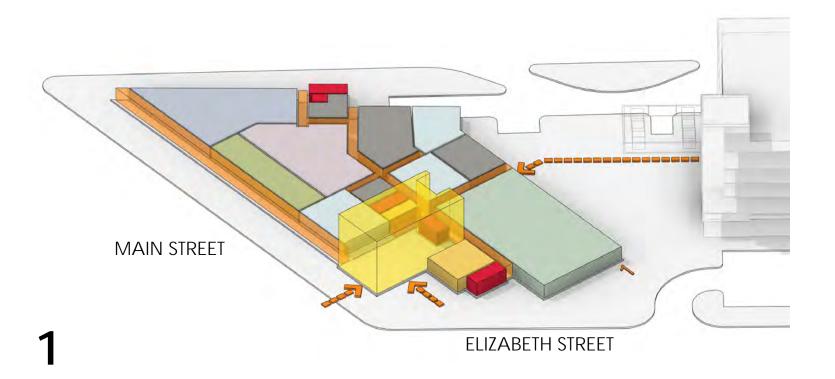

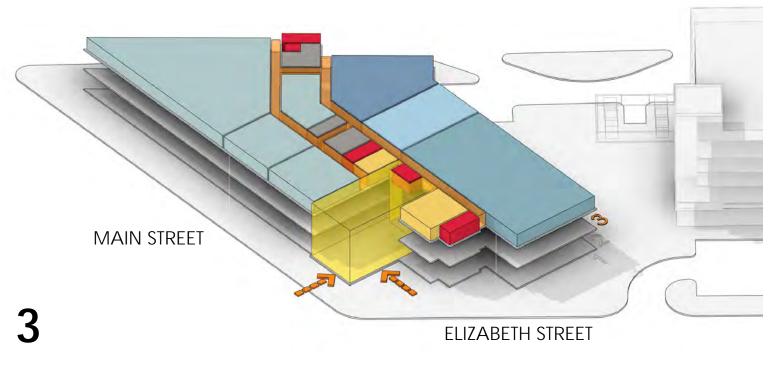


PLANNING CONCEPT DIAGRAMS







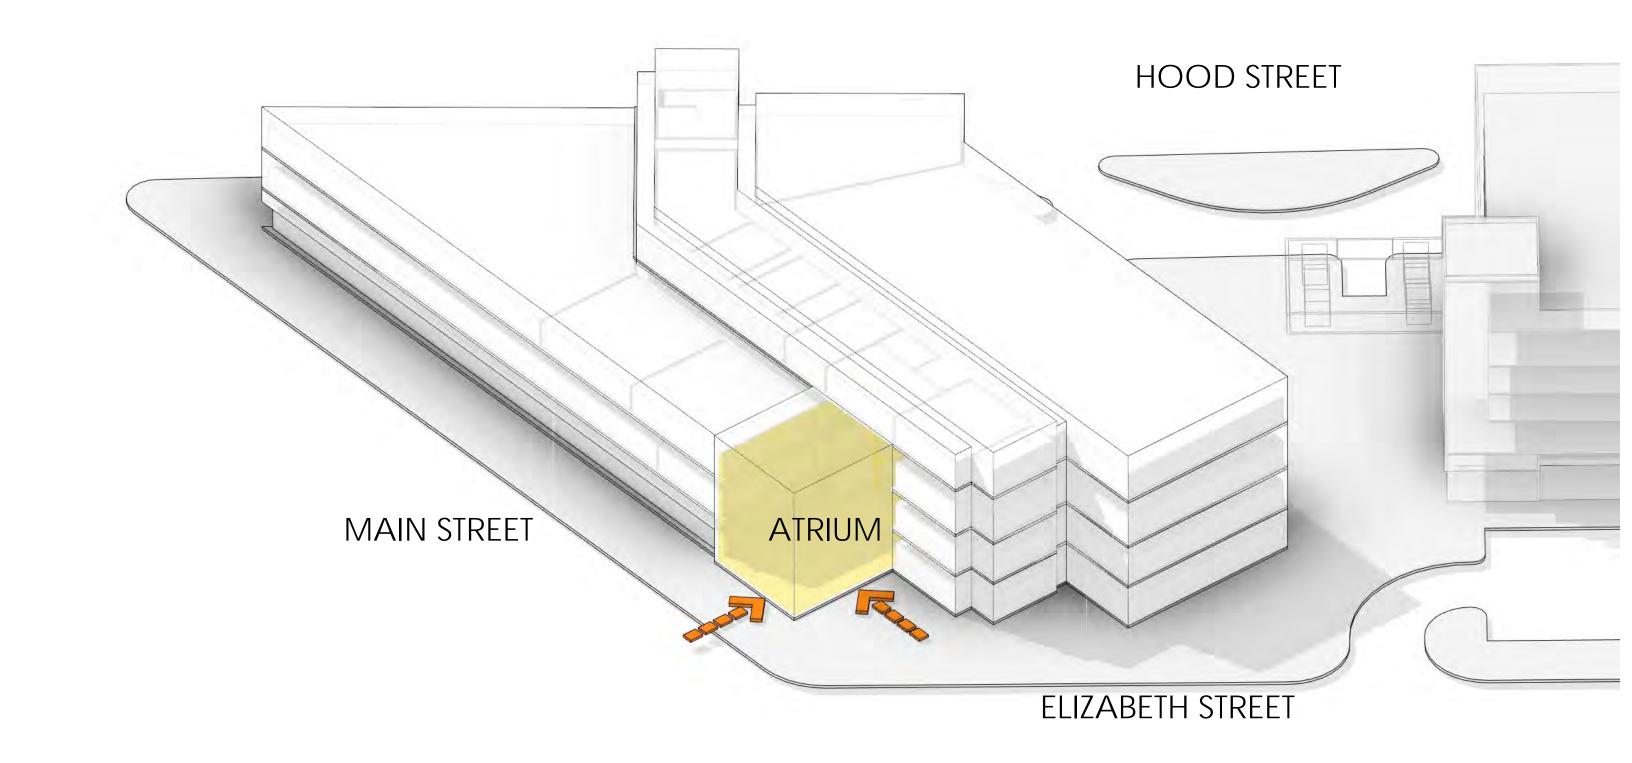

MASSING DIAGRAM







CONTEXT SURROUNDINGS



GOVERNMENT RESIDENTIAL MIXED USE

CONTEXT SCALE & TEXTURE



KRESS HILL / 21C HSB / THE DURHAM DVIII DPAC









VIEW FROM DOWNTOWN









VIEW FROM EAST DURHAM









BIRD'S EYE VIEW







VIEW FROM MAIN STREET









VIEW FROM EAST DURHAM

















DARK GREY BRICK

BASIS OF DESIGN: CAROLINA CERAMICS BLUE BLACK BLEND















LIGHT GREY BRICK BASIS OF DESIGN: Acme Brick Marble Grey




















METAL PANEL

BASIS OF DESIGN: Ti Coated Stainless







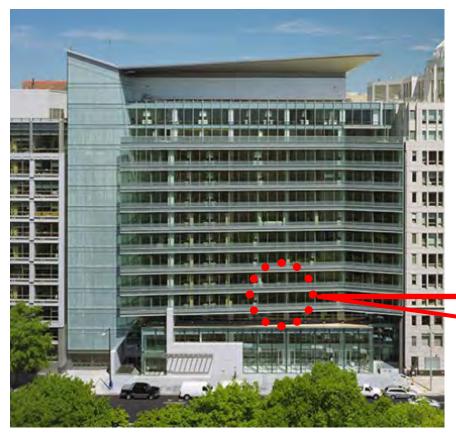








GLASS @ ATRIUM and MAIN STREET

BASIS OF DESIGN: VIRACON VE 1-85







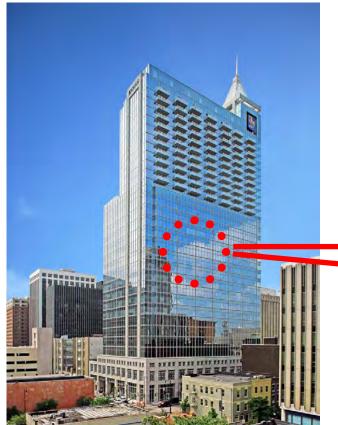








GLASS @ THE UPPER FLOORS

BASIS OF DESIGN: VIRACON VE 1-85








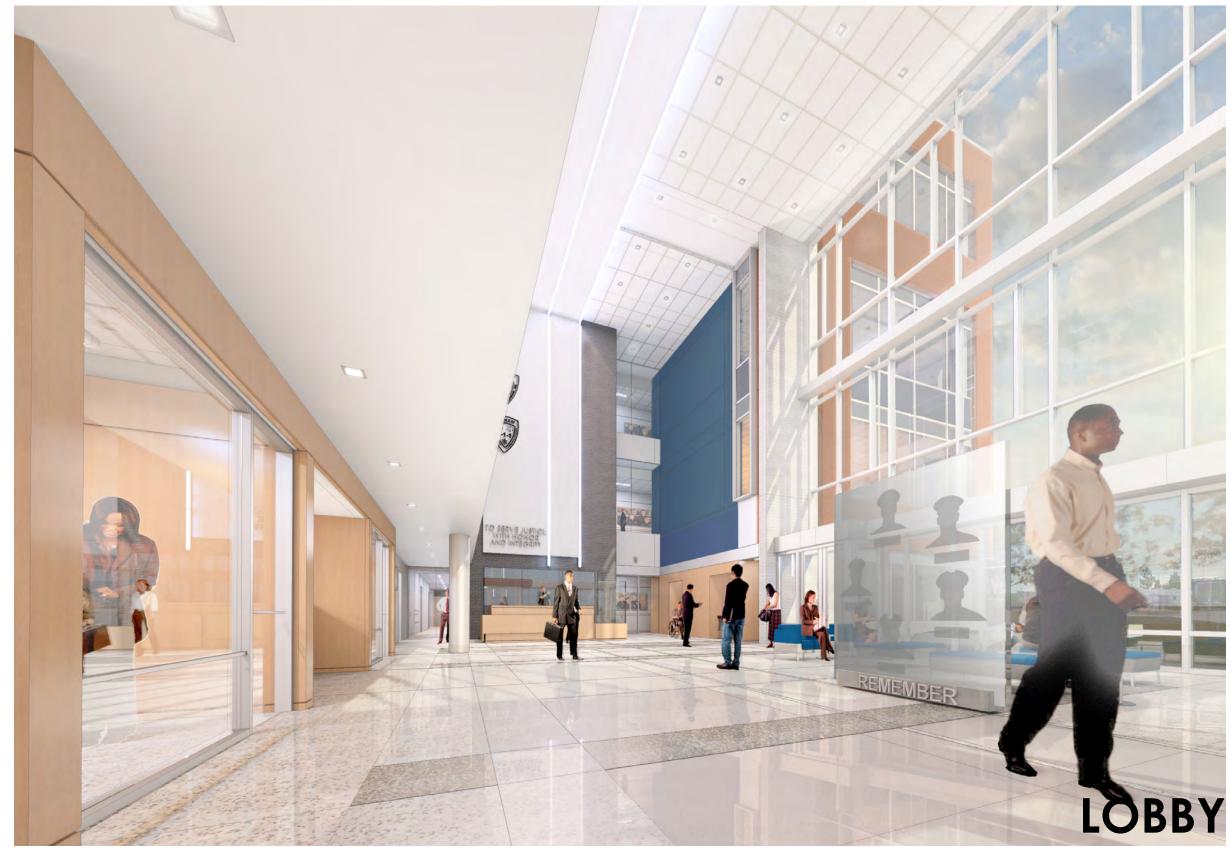








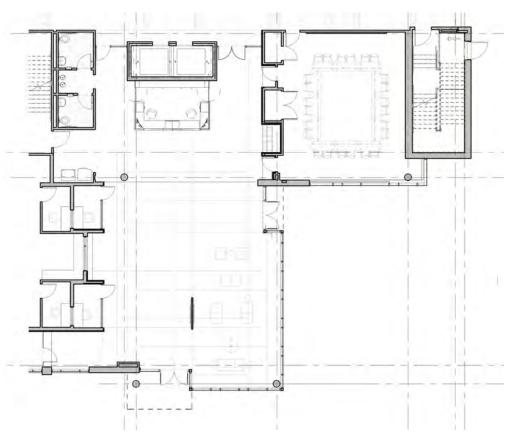

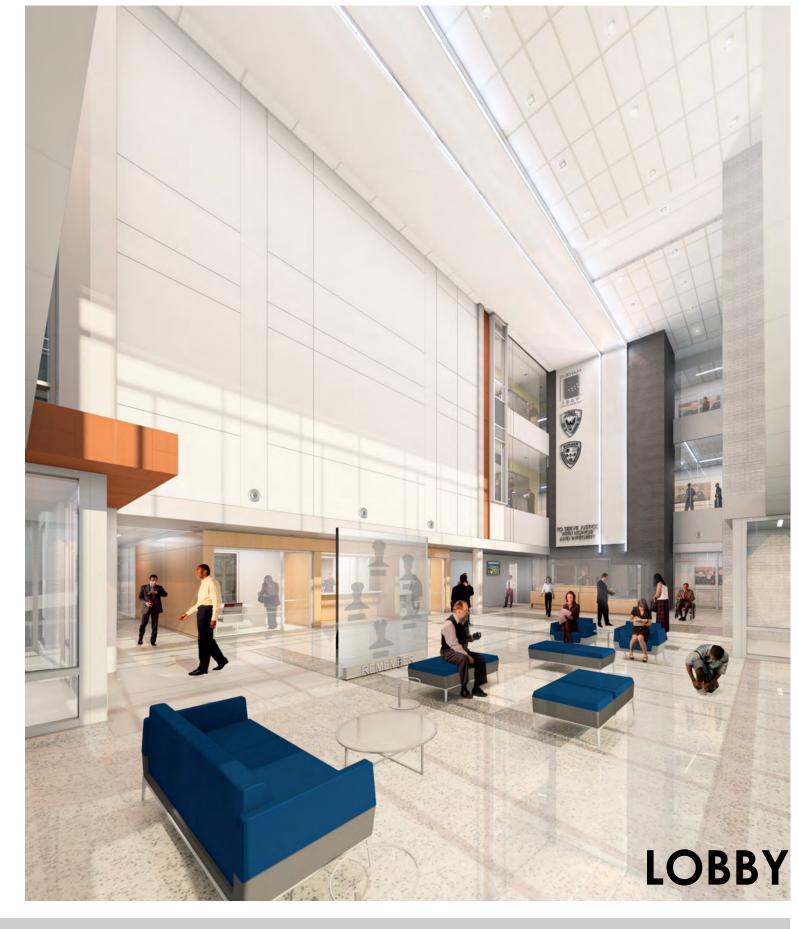















PROJECT COST

	Preliminary			
Bid Package	Guaranteed	Guaranteed	Variance	% (under)/over
	Maximum Price	Maximum Price		budget
1	\$2,145,853	\$1,547,359	(\$598,494)	28%
2	\$14,978,310			
Total Phase 1 & 2	\$17,124,163	\$1,547,359	(\$598,494)	

- Variance Under-run added to Bid Package 3 Budget
- Bid Package 3 is final Bid Package
- 50% CD (Construction Document) Estimate is the most current for Bid Package 3
- 50% CD Reconciled Estimate equals Current Budget \$49,647,359*
 - * includes \$272,927 of abatement escrow funds
 - * includes \$1,509,675 of design/estimating contingency







PHASE 1 UBE UPDATE

Cost of Work - \$865,720 **UBE Participation – 100%**

Trifecta Service Company (\$720,324) - Asian American KWD Contracting Group (\$145,396) - African American, Women Owned

Callis Contractors (CM Partner) - African American Allieway Marketing (Website Design) - Women Owned

3 jobs posted with NCWorks, 1 position filled Average daily workforce - 12







CONSTRUCTION UPDATE

PHASE 1 (DEMOLITION)

- Mobilized to site on July 25
- All hazardous material abatement completed
- Soil remediation has begun

PHASE 2 (STRUCTURE)

- Bid opened
- Conducting scope reviews and evaluations
- Mid-October target for foundation start
- January start of structural steel

PHASE 3 (BUILDING)

- Receiving and evaluating subcontractor prequalifications
- UBE information session on September 8
- Mid-September to mid-November bidding period







NEXT STEPS

Ongoing Site Planning Review Process

Demolition/Abatement/Environmental Work Ongoing

Completion of Construction Documents Phase September 30

Construction Begins Fall 2016

Construction Completion Summer 2018









